



BALE FEEDERS / ATTACHMENTS
PRE - DELIVERY INSPECTION CHECKLIST

Dealer: _____

Machine: _____

Serial Number: _____

Date: _____

CHECKS	DONE	N/A	COMMENT
--------	------	-----	---------

- Run Machine/Check Operation
- Check For Oil Leaks
- Check Hydraulic Hoses
- Check Chain Tensions
- Check Joystick Functions
- Check Grub Screws on Bearings
- Check Tyne Orientation is correct
- Torque Tynes
- Grease Machine
- Grease Wheel Bearings
- Set Tyre Pressures
- Lubricate Chains
- Torque Wheel Nuts
- Torque Swift Hitch Pin
- Torque Tow Eye

DONE	N/A	COMMENT

** NOTE: If machine is going to be stored, ensure hydraulic cylinder spears are lubricated/soft sealed**

Technician Name: _____


Technician Signature: _____

Completed check sheets are to be loaded with each warranty registrations to activate the machines 5 year warranty.

Bolt Torque Settings/Gear Oil	
Drawbar Bolts	200 N.m
Tyne Nuts	600 N.m
Axle Wheel Nuts	220 N.m
Swift Hitch Pin Nut	900 N.m

Tyne Installation:

When installing tynes in the 3PTL frame, please ensure the bale tynes are installed with the I Beam Profile standing upright like this:

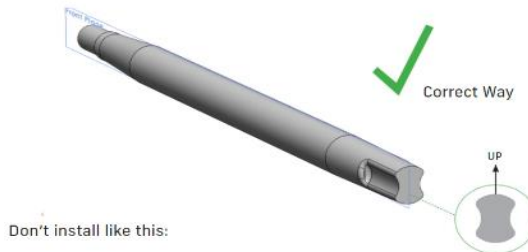

Don't install like this:

